


ID	WBS	Task Name	Lead	Work	Start	Finish	Successors	Predecessors	2007												2008											
									M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A
0	0	NGAO System Design Phase Schedule		15,840 hrs	Wed 6/21/06	Thu 4/17/08																										
1	1	SD Phase Management	PW	2,164 hrs	Wed 6/21/06	Thu 4/17/08																										
2	1.1	Planning and Contracting	PW	230 hrs	Wed 6/21/06	Thu 11/29/07																										
3	1.1.1	NGAO Proposal to SSC		0 hrs	Wed 6/21/06	Wed 6/21/06	4																									
4	1.1.2	Management Structure Decision by Directors		0 hrs	Fri 7/14/06	Fri 7/14/06	5	3																								
5	1.1.3	SD Phase System Engineering Management Plan	PW	80 hrs	Fri 9/1/06	Fri 9/29/06	4																									
6	1.1.4	SD Phase Contracts Generated	PW	60 hrs	Wed 9/27/06	Fri 10/27/06	8																									
7	1.1.5	Director Approval		0 hrs	Mon 10/9/06	Mon 10/9/06	40FS+3 wks																									
8	1.1.6	SD Partner Contracts Issued	PW	0 hrs	Fri 10/27/06	Fri 10/27/06	6,7																									
9	1.1.7	Mid-year Replan	PW	40 hrs	Mon 3/19/07	Tue 3/27/07																										
10	1.1.8	FY08 Replan	PW	50 hrs	Mon 11/12/07	Thu 11/29/07	371																									
11	1.2	Project Meetings		1,352 hrs	Wed 6/21/06	Wed 4/2/08																										
12	1.2.1	Executive Committee Telecons	PW...	360 hrs	Wed 6/21/06	Wed 4/2/08																										
13	1.2.2	Science Advisory Committee Telecons	CM	40 hrs	Mon 10/2/06	Thu 3/27/08																										
14	1.2.3	Team Meetings		952 hrs	Thu 9/14/06	Wed 1/9/08																										
15	1.2.3.1	Team Meeting #1 (mgmt, science & technical - Ir		68 hrs	Thu 9/14/06	Thu 9/14/06																										
16	1.2.3.2	Team Meeting #2 (CIT)		80 hrs	Tue 11/14/06	Tue 11/14/06																										
17	1.2.3.3	Team Videocon #3		44 hrs	Wed 12/13/06	Wed 12/13/06																										
18	1.2.3.4	Team Meeting #4 (Keck)		80 hrs	Mon 1/22/07	Mon 1/22/07																										
19	1.2.3.5	Team Videocon #5		44 hrs	Wed 3/7/07	Wed 3/7/07																										
20	1.2.3.6	Team Meeting #6 (UCSC)		80 hrs	Wed 4/25/07	Thu 4/26/07																										
21	1.2.3.7	Team Videocon #7		44 hrs	Wed 5/30/07	Wed 5/30/07																										
22	1.2.3.8	Team Retreat #8 (UCSC)		220 hrs	Mon 7/9/07	Wed 7/11/07	1FS+55 days																									
23	1.2.3.9	Team Videocon #9		44 hrs	Wed 8/22/07	Wed 8/22/07																										
24	1.2.3.10	Team Meeting #10 (CIT)		80 hrs	Tue 9/11/07	Tue 9/11/07																										
25	1.2.3.11	Team Videocon #11		44 hrs	Mon 11/5/07	Mon 11/5/07																										
26	1.2.3.12	Team Meeting #12 (Keck)		80 hrs	Wed 12/12/07	Wed 12/12/07																										
27	1.2.3.13	Team Videocon #13		44 hrs	Wed 1/9/08	Wed 1/9/08																										
28	1.3	Tracking and Reporting	PW	120 hrs	Sat 9/16/06	Thu 4/3/08																										
29	1.3.1	Report Preparation/Presentation	PW	120 hrs	Mon 10/2/06	Tue 12/11/07																										
30	1.3.2	Keck Science Meeting 06 (UCI)		0 hrs	Sat 9/16/06	Sat 9/16/06																										
31	1.3.3	SSC meeting (UCLA)		0 hrs	Mon 11/6/06	Mon 11/6/06																										
32	1.3.4	SSC meeting (Keck)		0 hrs	Wed 1/24/07	Wed 1/24/07																										
33	1.3.5	SSC meeting (CA)		0 hrs	Tue 4/3/07	Tue 4/3/07																										
34	1.3.6	SSC meeting (Keck)		0 hrs	Wed 6/20/07	Wed 6/20/07																										
35	1.3.7	Keck Science Meeting 07		0 hrs	Sat 9/15/07	Sat 9/15/07																										
36	1.3.8	SSC meeting (CA)		0 hrs	Tue 11/6/07	Tue 11/6/07																										
37	1.3.9	SSC meeting (Keck)		0 hrs	Thu 1/24/08	Thu 1/24/08																										
38	1.3.10	SSC meeting (CA)		0 hrs	Thu 4/3/08	Thu 4/3/08																										
39	1.4	Proposals & Fundraising		0 hrs	Fri 10/27/06	Mon 1/1/07																										
40	1.4.1	Dates & deliverables identified by Directors		0 hrs	Fri 10/27/06	Fri 10/27/06	41	7FS+3 wks																								
41	1.4.2	Support Advancement Office		0 hrs	Mon 1/1/07	Mon 1/1/07	40																									
42	1.5	System Design Report & Review	SA	462 hrs	Mon 10/1/07	Thu 4/17/08																										
43	1.5.1	System Design Report	PW	40 hrs	Wed 2/20/08	Mon 3/3/08	46,48	389,366,130																								

Project: NGAO System Design Phase
Date: Tue 5/22/07

Critical		Task		Baseline		Milestone		Project Summary		Deadline	
Critical Split		Split		Baseline Split		Summary Progress		External Tasks			
Critical Progress		Task Progress		Baseline Milestone		Summary		External Milestone			

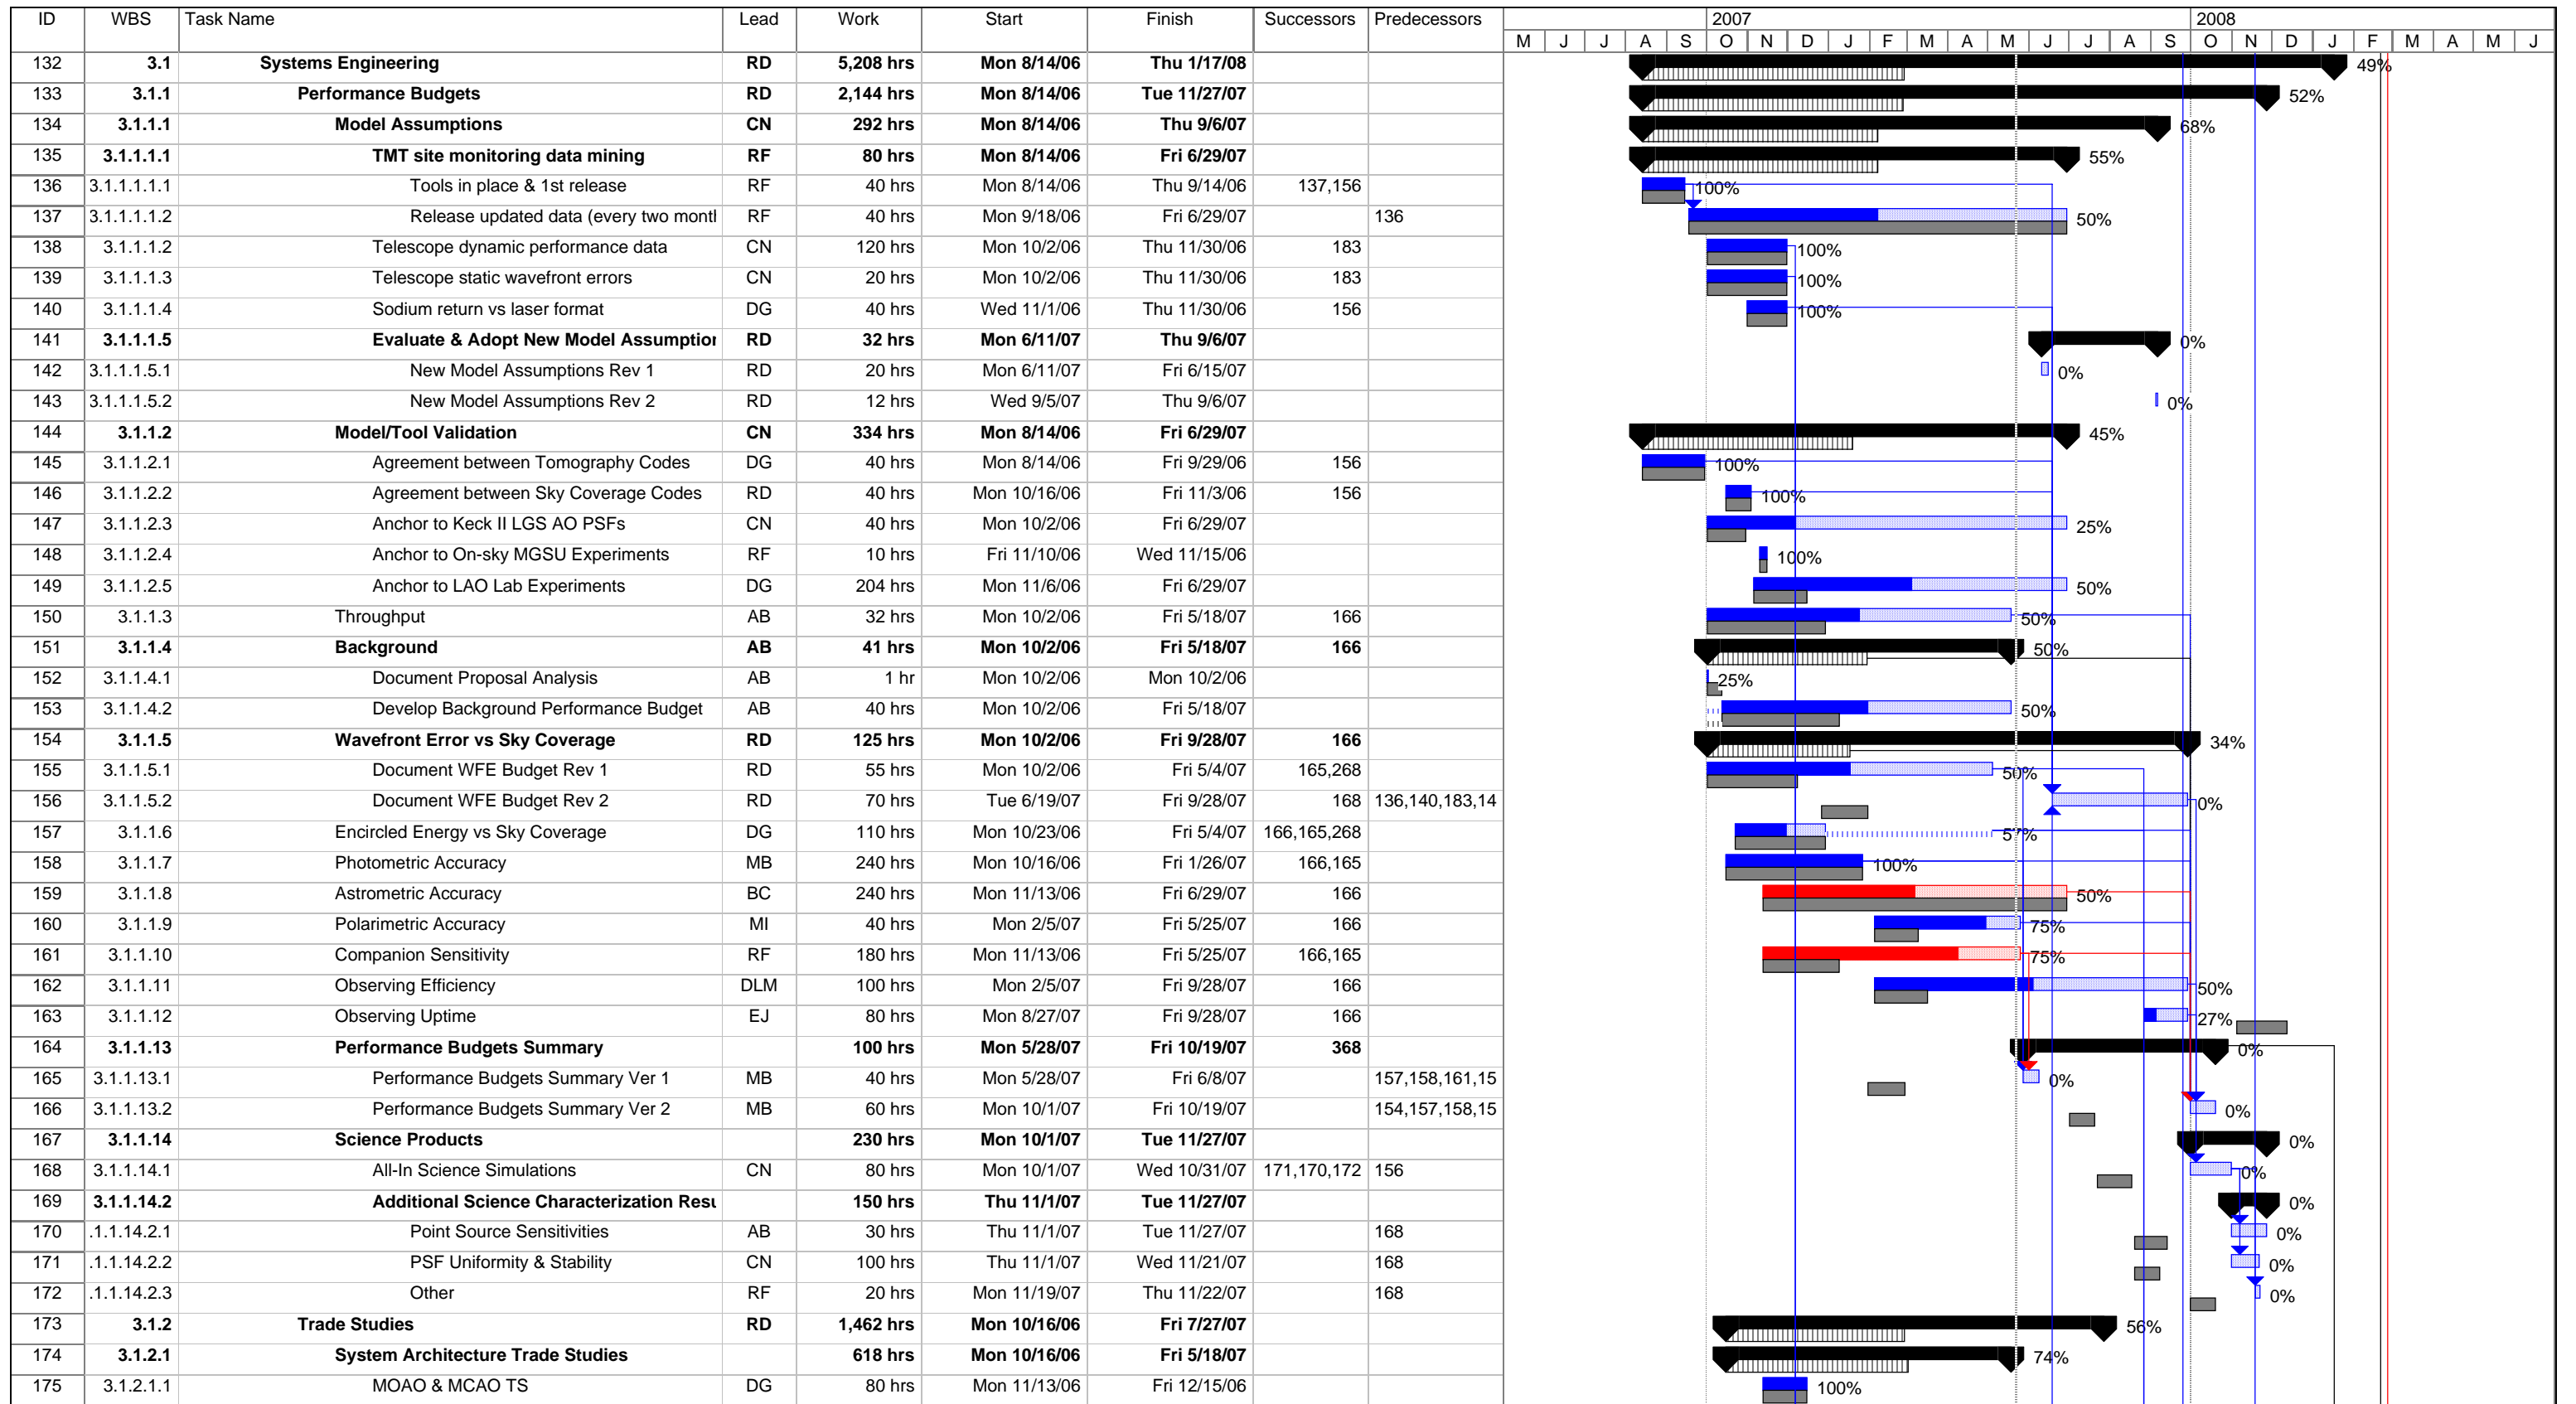

Project: NGAO System Design Phase
Date: Tue 5/22/07



