


ID	Task Name	Duration	Start	Finish	Predecessors	% Complete	Cost	Jul 16	Jul 23	Jul 30	Aug 6	Aug 13	Aug 20	Aug 27	Sep 3	Sep 10
								T	T	S	M	W	F	S	T	T
1	Palomar LGS	33 d	7/23/06	9/7/06		29%	\$15,933.78									
2	Laser	33 d	7/23/06	9/7/06		29%	\$15,933.78									
3	Operations	4 d	9/1/06	9/7/06		0%	\$0.00									
4	Pre-run checkout	3 d	9/1/06	9/3/06	21	0%	\$0.00									
5	LGS run support	3 d	9/5/06	9/7/06	4	0%	\$0.00									
6	Power upgrade	29 d	7/23/06	8/31/06		36%	\$15,933.78									
7	Preparation	7 d	7/25/06	8/2/06		100%	\$0.00									
8	Order remaining items	1 d	7/25/06	7/25/06		100%	\$0.00									
9	Prepare laser and downstairs lab	2 d	7/26/06	7/27/06	8	100%	\$0.00									
10	Move bench to laser lab	1 d	8/2/06	8/2/06	9	100%	\$0.00									
11	Gain module assembly	10 d	7/31/06	8/11/06		36%	\$0.00									
12	Machine parts	5 d	7/31/06	8/4/06		100%	\$0.00									
13	Assemble spare head	5 d	8/7/06	8/11/06	12	0%	\$0.00									
14	YAG delivery (latest possible)	0 d	8/8/06	8/8/06		0%	\$0.00									
15	Assemble 2 new heads	4 d	8/8/06	8/11/06	14,12	0%	\$0.00									
16	Gain module testing	14 d	8/13/06	8/31/06		0%	\$0.00									
17	Rebuild alignment system	1 d	8/13/06	8/13/06	10	0%	\$0.00									
18	Install new heads	2 d	8/14/06	8/15/06	17	0%	\$0.00									
19	Test power supplies and diodes	1 d	8/16/06	8/16/06	18	0%	\$0.00									
20	Test gain modules	2 d	8/17/06	8/18/06	19	0%	\$0.00									
21	Move bench back to AO lab	1 d	8/31/06	8/31/06	20	0%	\$0.00									
22	Procurement	12 d	7/23/06	8/9/06		100%	\$15,933.78									

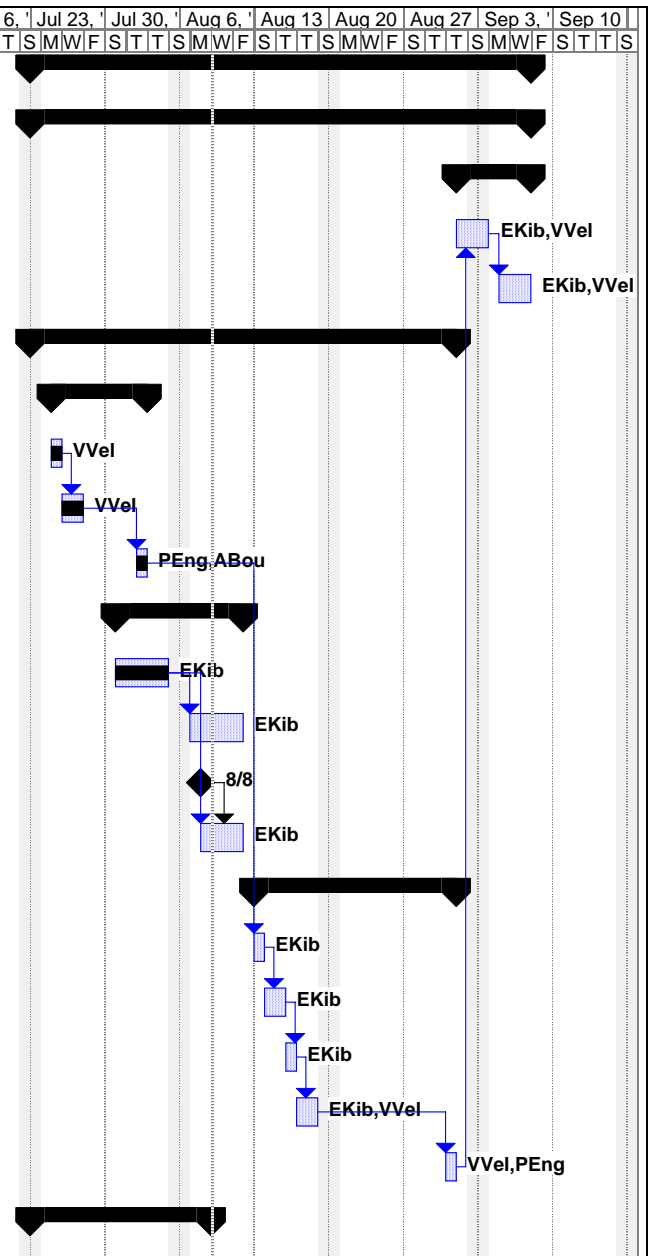

Project: laser_060809
Date: 8/9/06

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline
